SMART 16430

Novato (Grant) Platform Preliminary Schedule
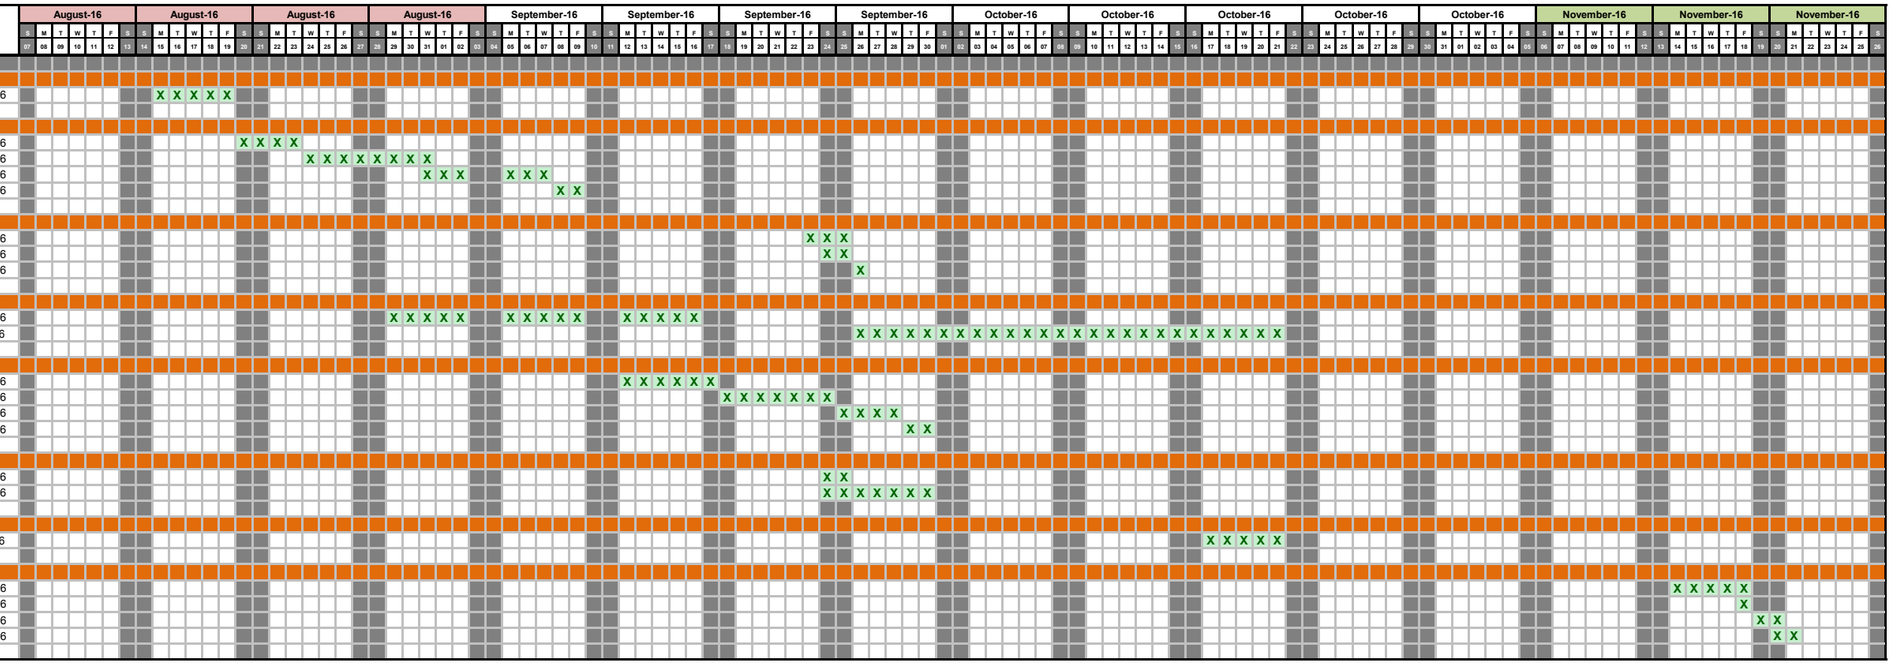
Activity Name	Start	Finish
SITE PREP AND SURVEY		
SITE/YARD PREP	15 Aug 16	19 Aug 16
PLATFORM FOOTINGS AND STEM WALLS (Week Days & Weekend Days)		
EXCAVATE AND GRADE FOR FOOTINGS	22 Aug 16	23 Aug 16
F/P/S FOOTINGS	24 Aug 16	31 Aug 16
F/P/S STEM WALLS	31 Aug 16	07 Sep 16
BACKFILL STEM WALL	08 Sep 16	09 Sep 16
TRACKWORK Phase I (Shutdown FRI 10 AM - MON 4 AM)		
DEMO EXISTING TRACKWORK	23 Sep 16	25 Sep 16
INSTALL GAUNTLET TRACK RUN	24 Sep 16	25 Sep 16
WELD, TAMP, REGULATE GAUNTLET TRACK RUN	25 Sep 16	26 Sep 16
PLATFORM DECK (Week Days & Weekend Days)		
INSTALL CONDUITS	29 Aug 16	16 Sep 16
F/P/S DECK	26 Sep 16	21 Oct 16
RAMP (Week Days & Weekend Days)		
EXCAVATE AND GRADE FOR FOOTINGS	12 Sep 16	17 Sep 16
F/P/S FOOTINGS & STEMS	18 Sep 16	24 Sep 16
F/P/S CAP	25 Sep 16	28 Sep 16
BACKFILL STEM WALL	29 Sep 16	30 Sep 16
Crossing Alterations (Weekend Days)		
INSTALL PANELS	24 Sep 16	25 Sep 16
INSTALL FLATWORK	24 Sep 16	30 Sep 16
Tactile Install (Week Days)		
DECK TACTILE SUB	17 Oct 16	21 Oct 16
TRACKWORK Phase II (Special Track Cut-in FRI 10 AM - MON 4 AM)		
PREP TURNOUT	14 Nov 16	18 Nov 16
DEMO EXISTING TRACKWORK	18 Nov 16	18 Nov 16
INSTALL GAUNTLET TURNOUTS	19 Nov 16	20 Nov 16
WELD, TAMP, REGULATE GAUNTLET TURNOUTS	20 Nov 16	21 Nov 16
